


Jurupa Valley Construction Updates: Riverside Transmission Reliability Project (RTRP)


Jurupa Valley City Council – September 18, 2025

Project Background

SCE and Riverside Public Utilities (RPU) have been working together on the Riverside Transmission Reliability Project (RTRP) for over 15 years. CAISO recognized the need for the project in 2006 and approved its construction that began this summer.

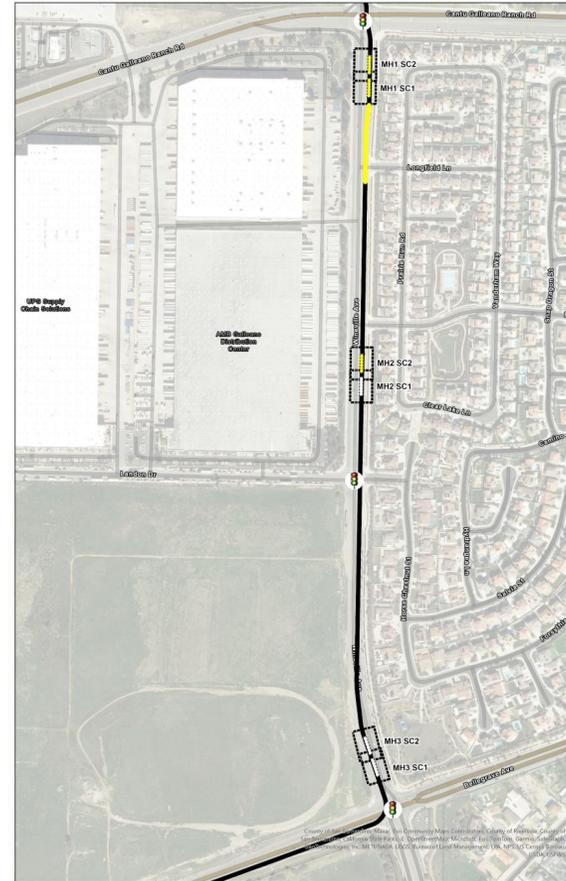

UG North

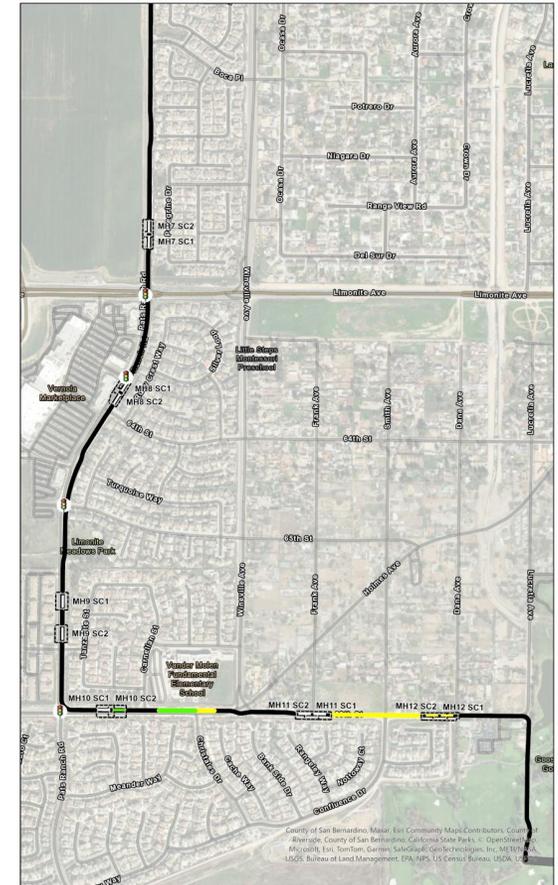

UG South

What's Going Well | Community Impacts

✓ 1. Coordination with the City

- Ongoing collaboration with the **City's Public Works Department, City Manager office, and Public Information.**

✓ 2. School District Coordination

- Ongoing communication with the VanderMolen school **principal** and **Corona-Norco Unified School District.**
- Construction activities are scheduled in alignment with the **district calendar**

✓ 3. Community Services District / Parks District

- Engagement initiated to drive alignment with local services and infrastructure needs.

✓ 4. Public Transportation


- **Initial outreach** to transit agencies is complete.
- **2026 work plan** is in development


✓ 5. Project-related Hotline activity is minimal

- Indicating effective communication and low disruption to residents.

✓ 6. Workforce & Local Economic Impact

- **Southern California subcontractors** are actively engaged.
- **85%** of workers live within 50 miles.
- Workers are **supporting local businesses.**

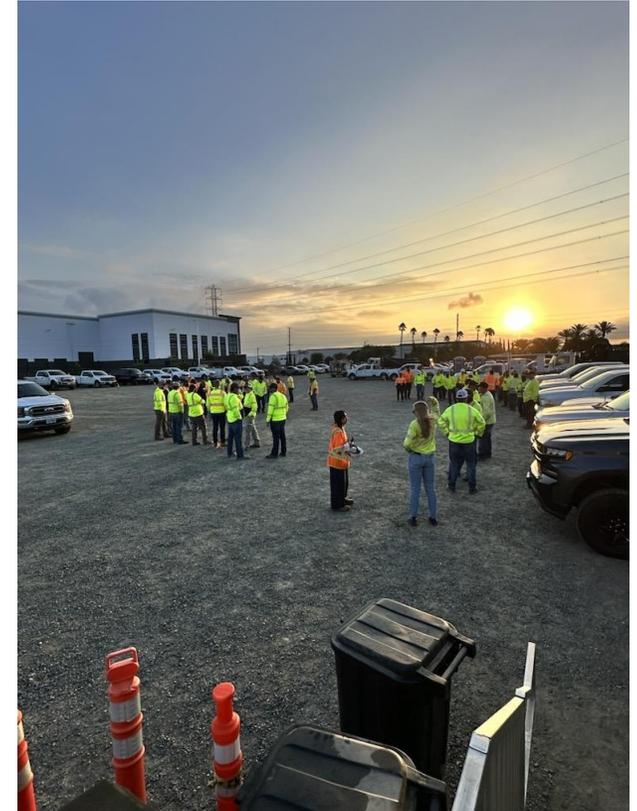

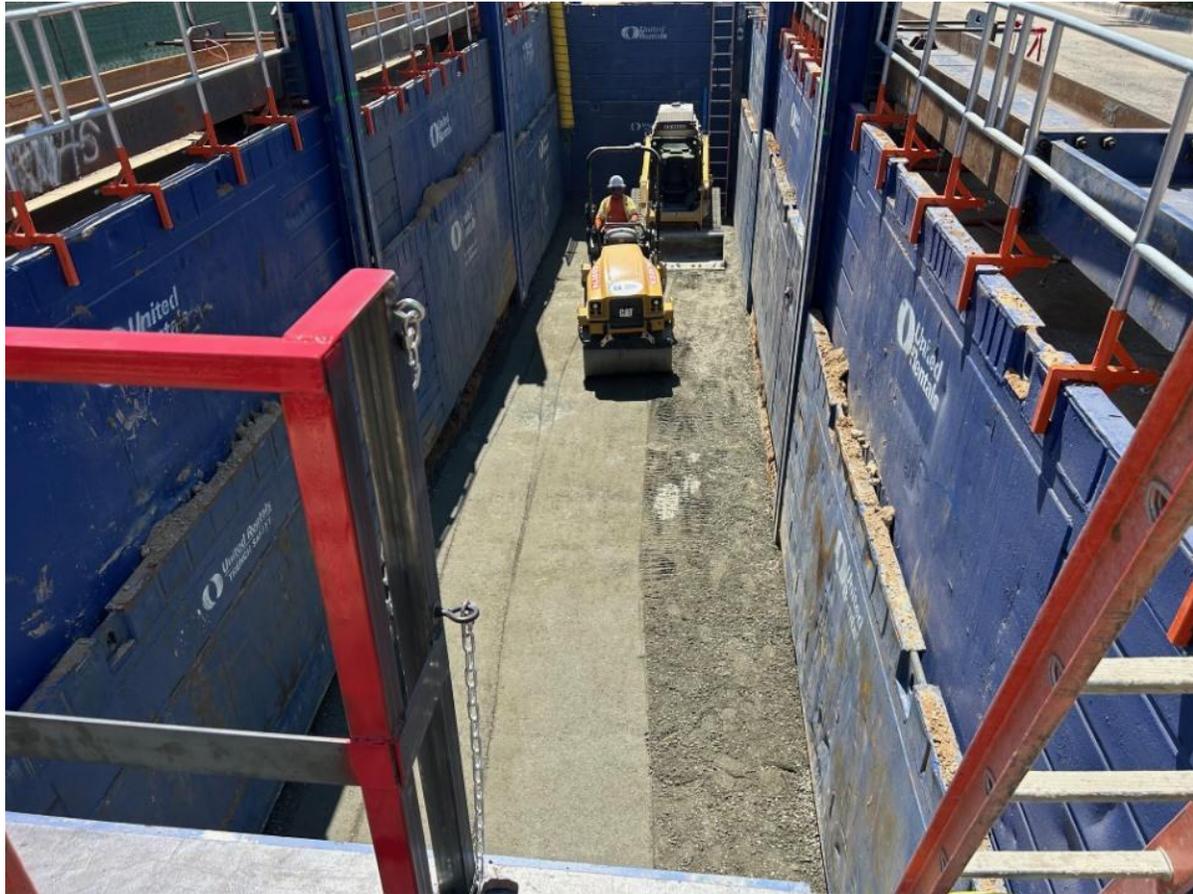

Project Photos: Vault preparation and trenching




Project Photos: Vault Installation



Project Photos: Vault Installation

Challenges | Opportunities for Lessons Learned

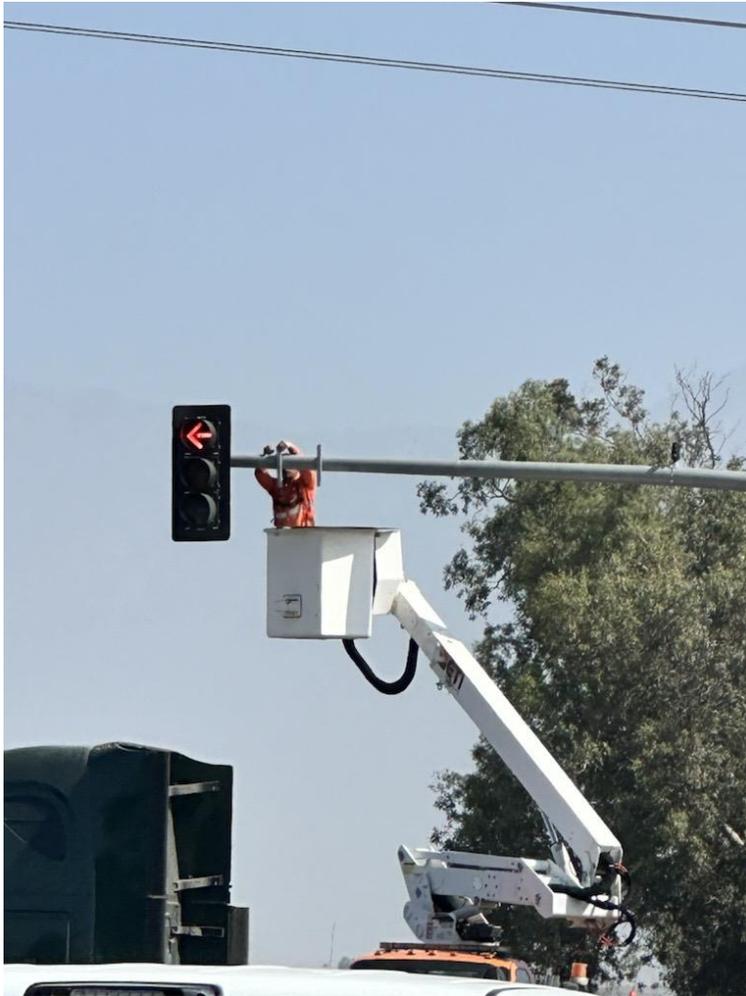

Sandy Soil Challenges

Sandy soil at the site compromises excavation stability, requiring soil stabilization and additional shoring measures.



Abandoned or Unexpected Utilities Issues

Undocumented abandoned utilities complicate installations, requiring careful mapping and coordination for safe removal or rerouting and adaptive planning.



Traffic Control Management

Managing traffic flow near the site requires detailed planning, signage, detours, and coordination with the City and County.

Wineville Avenue

Careful planning for major intersections

Temporary detours



Wineville Avenue to Pats Ranch Road

Coordination with Lennar




Pats Ranch Road to 68th St

Holiday period sensitivity



68th Street

School coordination

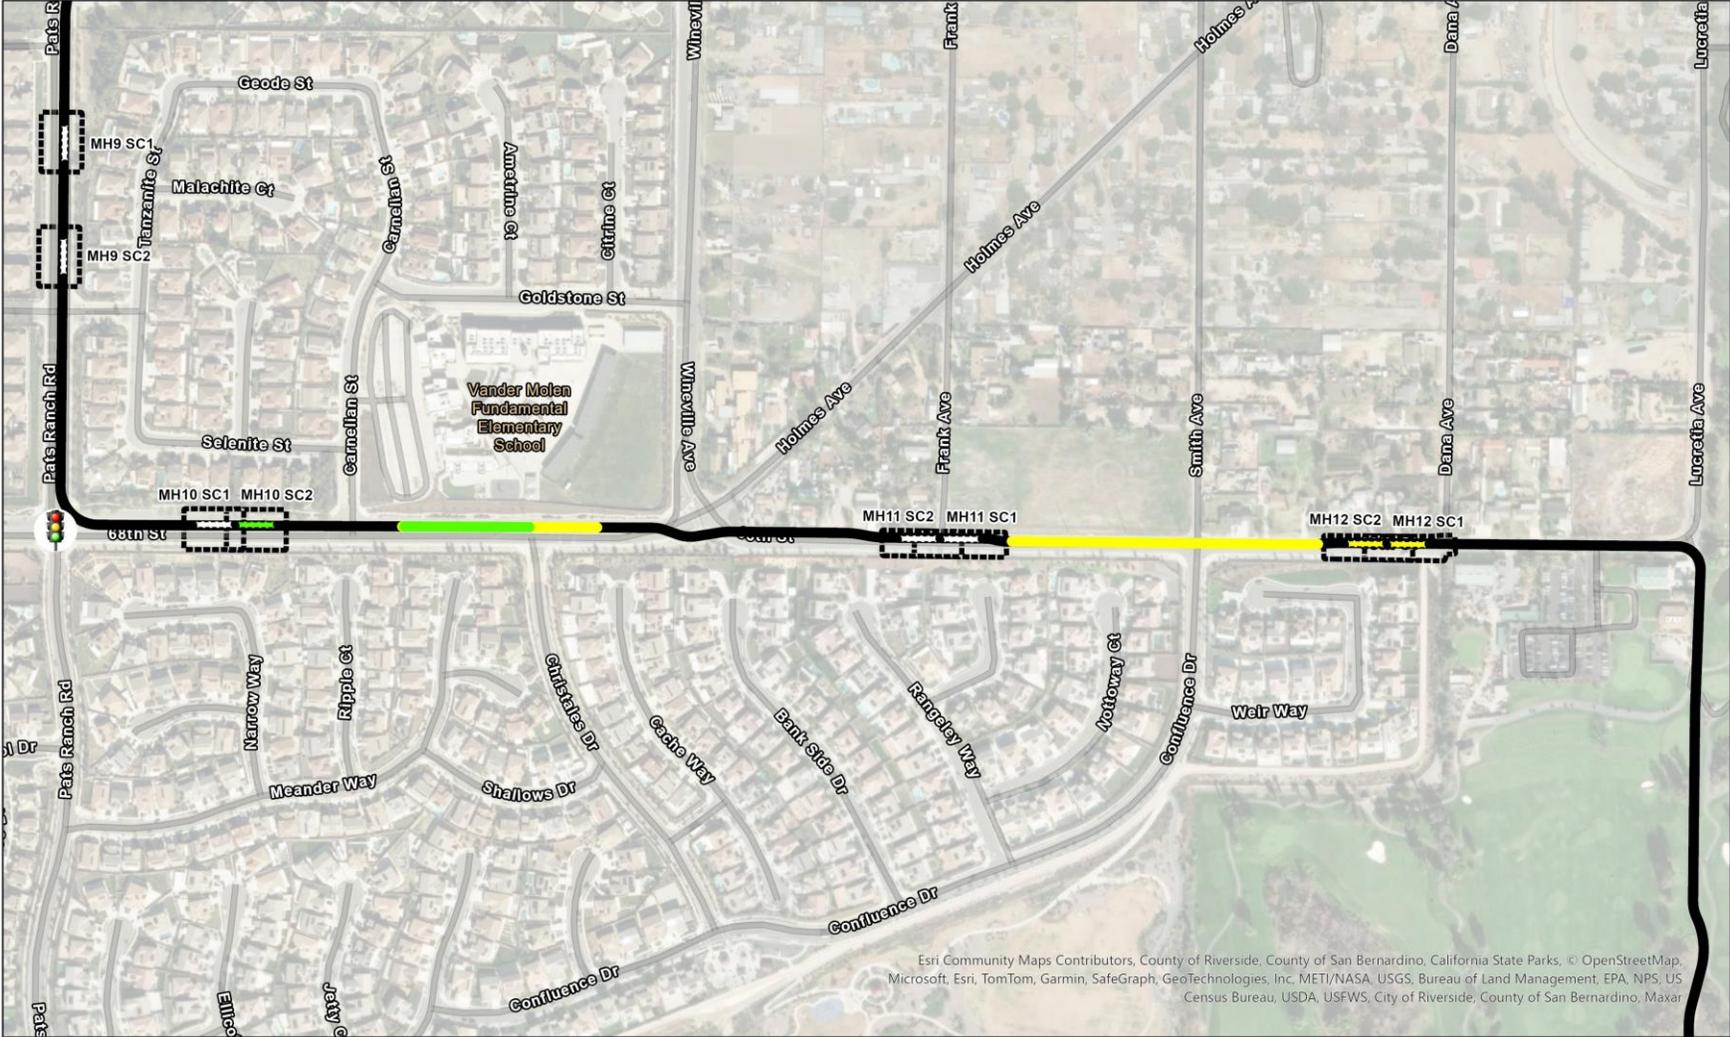

Esri Community Maps Contributors, County of Riverside, County of San Bernardino, California State Parks, © OpenStreetMap, Microsoft, Esri, TomTom, Garmin, SafeGraph, GeoTechnologies, Inc, METI/NASA, USGS, Bureau of Land Management, EPA, NPS, US Census Bureau, USDA, USFWS, City of Riverside, County of San Bernardino, Maxar

Continued Engagement | Key Communication Channels



Regular updates with the City of Jurupa Valley

- Bi-weekly coordination meetings
- Real-time collaboration and issue resolution



Engage with the Chamber of Commerce

- Regular briefings
- Business impact updates



Future City Council updates

- Milestone updates as needed



Traffic Control

- Continued coordination with City



Communication coordination with the City

- Notify the city when we will be distributing information



Project Webpage updates

- Provide project construction status in English and Spanish on sce.com/rtrp
